

SAFETY ALERT

INCIDENT	INOT962 - Plant Roll Over
SUBJECT	Excavator rolled onto its side
INCIDENT DATE	08.05.2020
BUSINESS UNIT	Infrastructure – NX2 Pūhoi to Warkworth Project


WHAT HAPPENED?

At Approximately 16:30 on Friday 8th of May an excavator was tracking a skip bin through site. During the operation his front right track has dropped into a hole, causing the excavator to roll onto its side.

No person was injured during the incident.

The incident scene was secured and worksafe were notified. The scene was released back to the control of the project team at 17:40.

An incident investigation is currently underway.

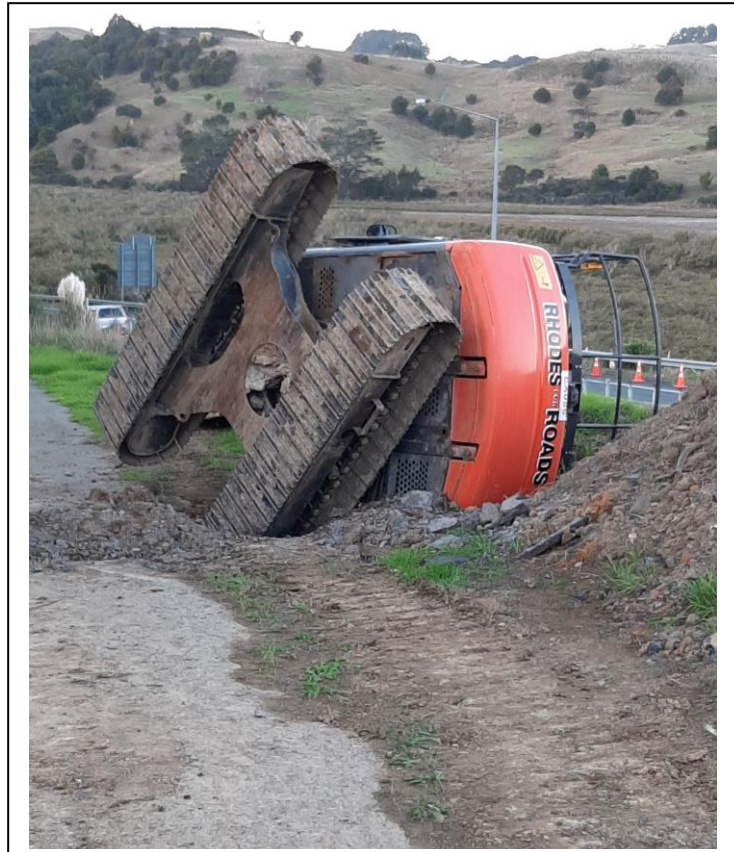

IMPORTANT REMINDER FOR ALL OF US (pre-investigation)

Always adhere to the Project Rules:

- Is the machine fit for purpose for the work task?
- Are open excavations barricaded or delineated?
- Is an approved lift plan in place for the activities?
- Are personnel trained and competent for the work activities?
- Does the JSEA detail the work activities and relevant controls?

FOR MORE INFORMATION, PLEASE CONTACT

Robert Jones, Project Director
 Robert.Jones@nx2.co.nz, +64 27 217 5344
